

REQUEST FOR INFORMATION (RFI)

PROJECT :	BKK2	R.F.I. NO. :	523213-01-RFI-AR-0019
TO :	CTA	ATTENTION :	CTA
SUBMITTED DATE:	14-Jan-26	NEED REPLY BY DATE :	21-Jan-26

SUBMISSION OF :	<input checked="" type="checkbox"/> Q&A	<input type="checkbox"/> Drawing	<input checked="" type="checkbox"/> Document	<input type="checkbox"/> Others (as specified below)
SUBJECT :	Request for Information - Clarification on Door Frame Depth Relative to Varying Wall Thicknesses			

Total Page (s) : **2** (Including this page)

FUNCTION :	<input type="checkbox"/> Structural (ST)	<input type="checkbox"/> Electrical & Communication (EL)	<input type="checkbox"/> Mechanical (ME)	<input type="checkbox"/> Vertical Transport (VT)
	<input checked="" type="checkbox"/> Architectural (AR)	<input type="checkbox"/> Fire Protection (FPI)	<input type="checkbox"/> Hydraulic & Sanitary (HY)	<input type="checkbox"/> Other (O)

(1) CONTRACTOR REQUEST FOR INFORMATION :

The current project specification states a standard door frame depth of 150 mm for all door types. However, based on the wall types and finishing schedules, the actual wall thicknesses vary across different areas as follows:

Block wall (double-sided finish): 170 mm

Block wall (single-sided finish / riser): 155 mm

Block wall (standard finish): 140 mm

Drywall partition: 136 mm

To ensure a flush and smooth finish, we would like to request approval for GAA to adjust the door frame depth to match and suit the specific wall thickness at each location (e.g., 140 mm, 170 mm, 155 mm, and 136 mm). Alternatively, please provide a standard detail for handling the variance (e.g., through specific casing or architrave details).

Requested by :

Engineering Manager

Reviewed by :

Project Manager

(2) ATTN : Commtech Asia (Thailand)

For Approval See Note Please Clarify

From : GAA Group

By :

Mr. Itsarate Trachuengtong/
Project Manager

Date : 14-Jan-26

Note :

As per the meeting between STT, CTA, Aurecon, SLA, GAA and TTI, GAA are to provide a typical detail for each door type for review by SLA.

Reviewed By : Commtech Asia (Thailand)

Name / Position Finlay Coady

Sr. Project Manager
21 January 2026

(3) ATTN : AURECON

For Approval See Note Please Clarify

From : Commtech Asia (Thailand)

By :

Name / Position ()

Date :

Note :

SLA: Please see detail 10, 17, 18, 19 per AR-9104 on sheet 3.

Reviewed By : Tarkoon Suwansukhum
AURECON

Name / Position (Tarkoon S / Architect)

Date : 29 January 2026

(4) ATTN : STT GDC

- Clarification only Not Approved
- Approved for proceeding work
- Approved with comments, proceeding work in compliance with comments
- Approved with comments, not for proceeding work and need to re-submit

From : AURECON

By :

Name / Position ()

Date :

Note :

Please follow consultant's comment and please provide enlarge details
in shop level detail for approval

Reviewed By : STT GDC

Name / Position Sirawit Thepsuwan VP PMO

Date : 5 Feb 2026

CC :

STT GDC

AURECON

Commtech Asia
(Thailand)

GAA

OTHERS.....

Appendix: A door schedule and door hardware (2025)

1. Door Schedule






Block Wall (double-sided finish 140mm thk.): 170mm

Block Wall (single-sided finish / Riser): 155mm

Block Wall (standard finish 90 mm thk.): 140mm

Drywall Partition: 136mm

DOOR SCHEDULE FLOOR PLAN															150 mm For All Door type	
Room No.	Room Name	Type Mark	Width	Height	Hard ware Set	Door hand-ing	Door closer	Door stop	Access control	Key group	Frame depth	STC rating	Mortise lock note	Note		
02-01-001	STAIR ST-6	-	-	-	-	-	-	-	-	-	-	-	-	-		
02-01-002	ENTRANCE	D1	10100	3000	A	SLIDING	NO	NO	NO		150					
02-01-003	RECEPTION HALL	D2	4000	3000	B	LHR.	YES	YES	NO		150					
02-01-004	SECURITYROOM 1	D3	1100	2100	C	RHR.	YES	YES	9		150					
02-01-005	HALL 1.1	D5	2500	3150	F	RHRA.	YES	NO	1		150					
		D5	2500	3150	F	RHRA.	YES	NO	5		150					
02-01-006	STAIR ST-1	D4	1000	2150	E	LH.	YES	YES	2		150					
		D4	1000	2150	E	LH.	YES	YES	7		150					
02-01-007	LIFT 1	-	-	-	-	-	-	-	-		-	-	-	-		
02-01-008	FIREMAN LIFT LOBBY	D29	1900	2850	AA	RHRA.	YES	NO	1		150					







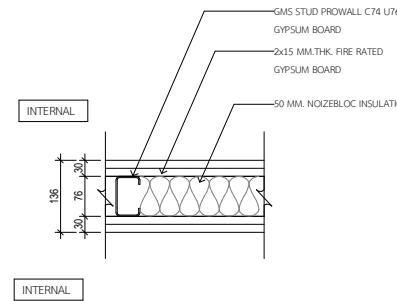
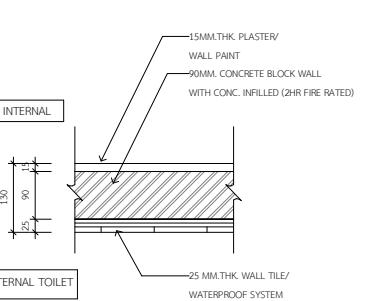
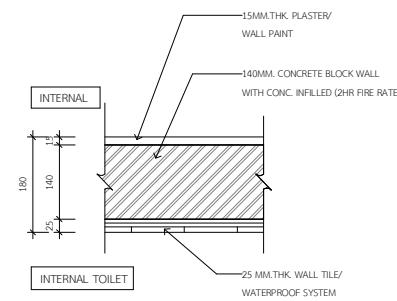
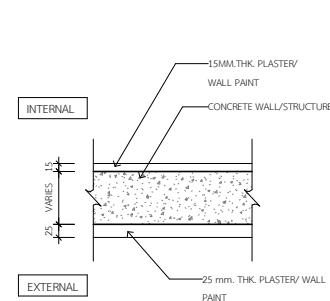


1 WALL MATERIAL 1

2 WALL MATERIAL 2

3 WALL MATERIAL 3

4 WALL MATERIAL 4

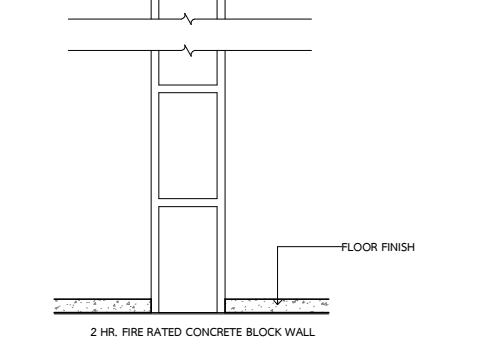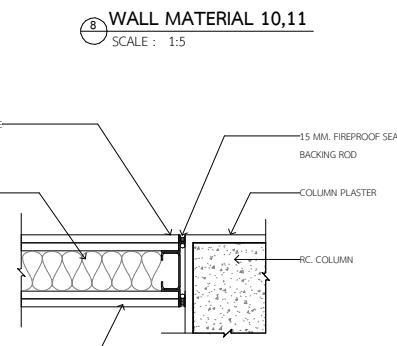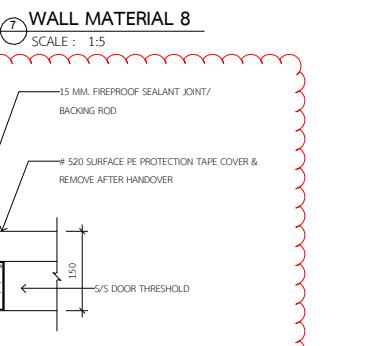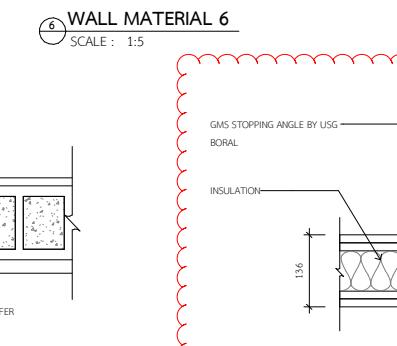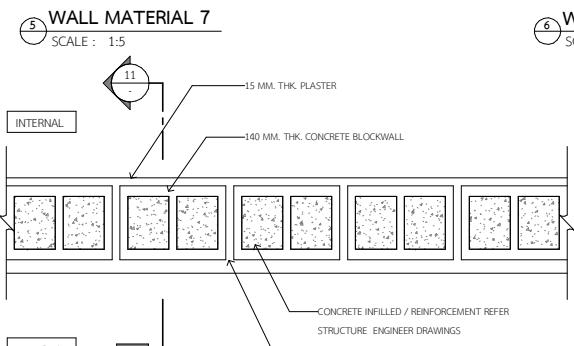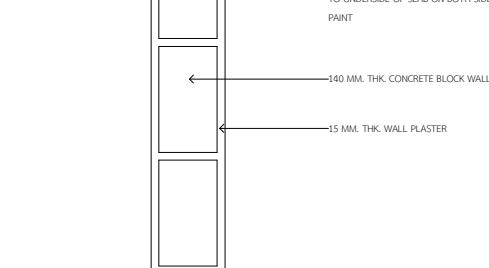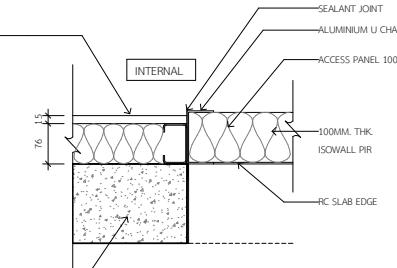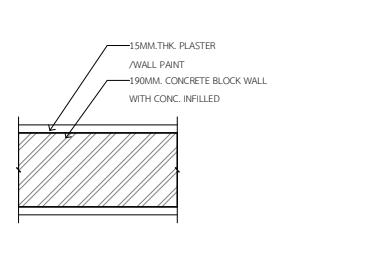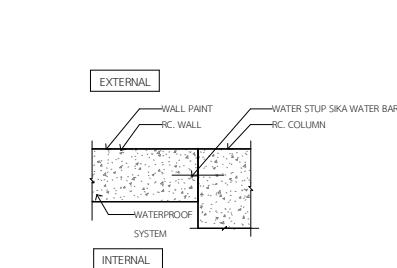
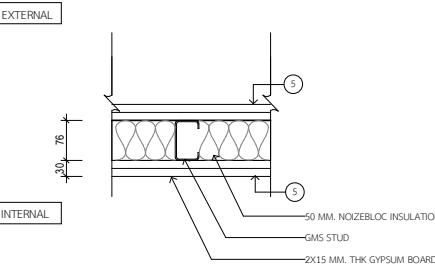


9 CONCRETE BLOCK 2 HR. FIRE RATED PLAN

10 TYPICAL WALL / DOOR JAMB DETAIL

11 TYPICAL WALL / COLUMN DETAIL

12 WALL SECTION AT TOP/BOTTOM



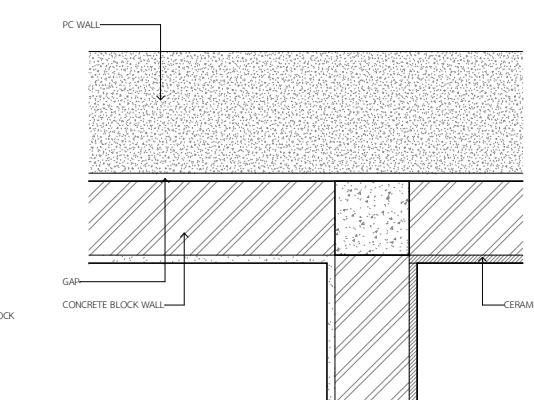
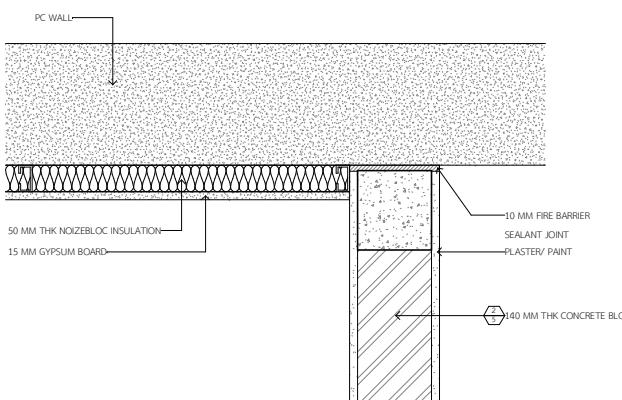


13 TYPICAL WALL DETAIL 2

14 TYPICAL WALL DETAIL 3

15 RC WALL JOINT DETAIL GROUND FLOOR

16 RC WALL JOINT DETAIL 2nd-6th FLOOR

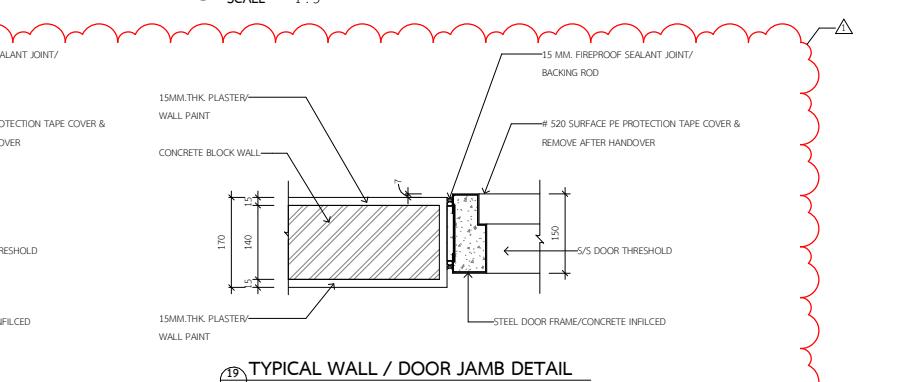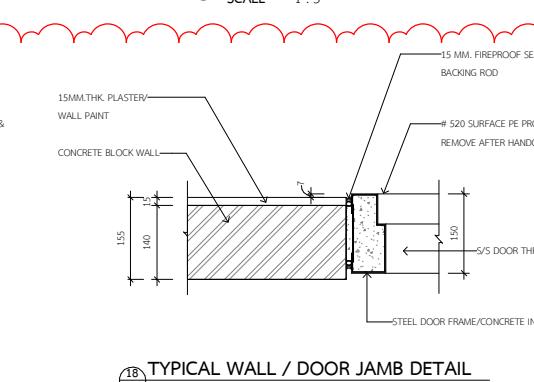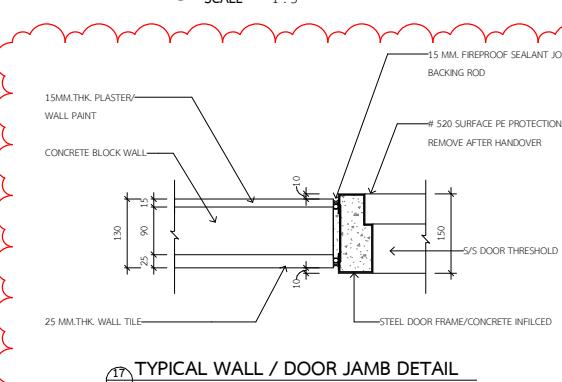

17 TYPICAL WALL / DOOR JAMB DETAIL

18 TYPICAL WALL / DOOR JAMB DETAIL

19 TYPICAL WALL / DOOR JAMB DETAIL

CLIENT
ST Telemedia Global Data Centres
STT GDC (THAILAND) CO., LTD.
945 Maitriworn Office Tower, 22nd+23rd Floor
Rama 4 Road, Wangmai, Pathumwan, Bangkok 10330

ENGINEER
aurecon
www.aurecongroup.com

STRUCTURAL REVIEWER

STRUCTURAL AND MECHANICAL

MECHANICAL AND COMMUNICATIONS

MECHANICAL

STRUCTURAL

MECHANICAL

STRUCTURAL AND MECHANICAL

STRUCTURAL

MECHANICAL
